GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : [illegible]

b) Location of the Site : Bratarayanapura [illegible]

c) Area of the land : Muneshwara Temple
Parrasenahalli

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss

2) Recommended Site for drilling : Ward No. 05

3) Total depth to be drilled : 1100' - 1220'

4) Approx. casing pipe required : 180' - 200'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 10 -

7) Qty. of water expected : 2 inch

8) Method of survey carried out : Geophysical method

9) Remarks : 6" / 12" Dia Drilling

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

BOREWELL SITE PLAN

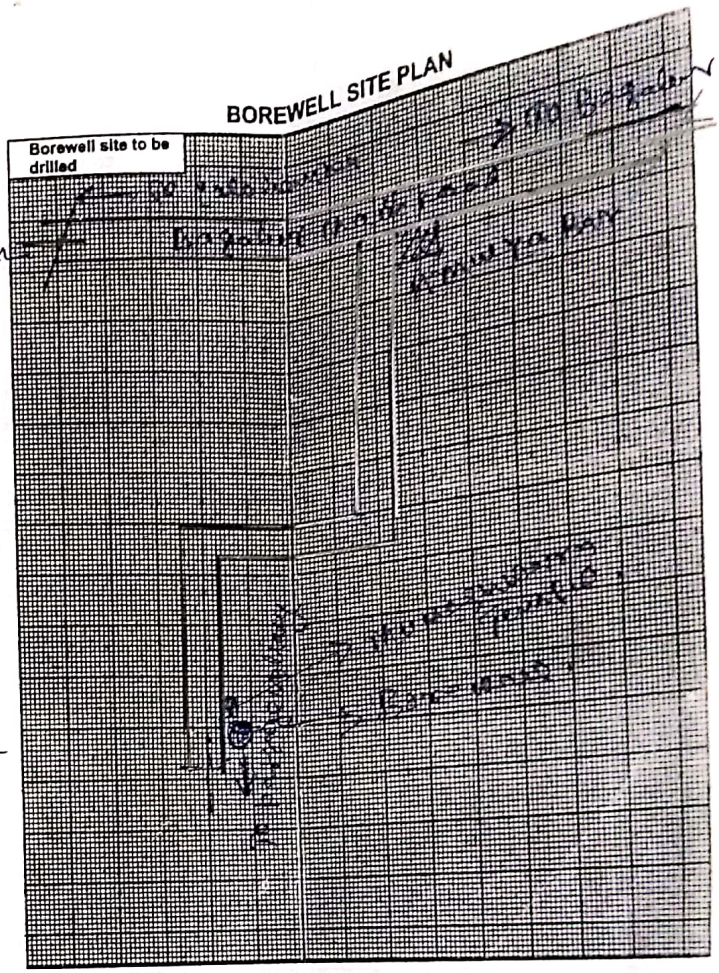

Scanned by CamScanner

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 675 Date : 21/10/2019

1. Customer's Name and Address with Telephone No. : AEE BBMP Byatarayanapura Sub Division

2. Well Location : Muneshwara Temple Kathrigenahally

3. Total Well Depth / Drilled in Ft. : 1214 feet.

4. Casing Erected in Ft. : 190 feet.

5. Water Struck at the Depth of : —

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear

8. At the Depth of : 1108 feet,

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathy

Manager / Proprietor

Party's Signature

Scanned by CamScanner

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP

b) Location of the Site : Byatarayanapura Sub

c) Area of the land : Ashoknagara Layout 11th Main

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Granite gneiss

2) Recommended Site for drilling : Ward no. 05

3) Total depth to be drilled : 1110' - 1220'

4) Approx. casing pipe required : 185' - 205'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 10 -

7) Qty. of water expected : 2 inch

8) Method of survey carried out : Geo mechanical

9) Remarks : 6 1/2' Dia Bore well

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

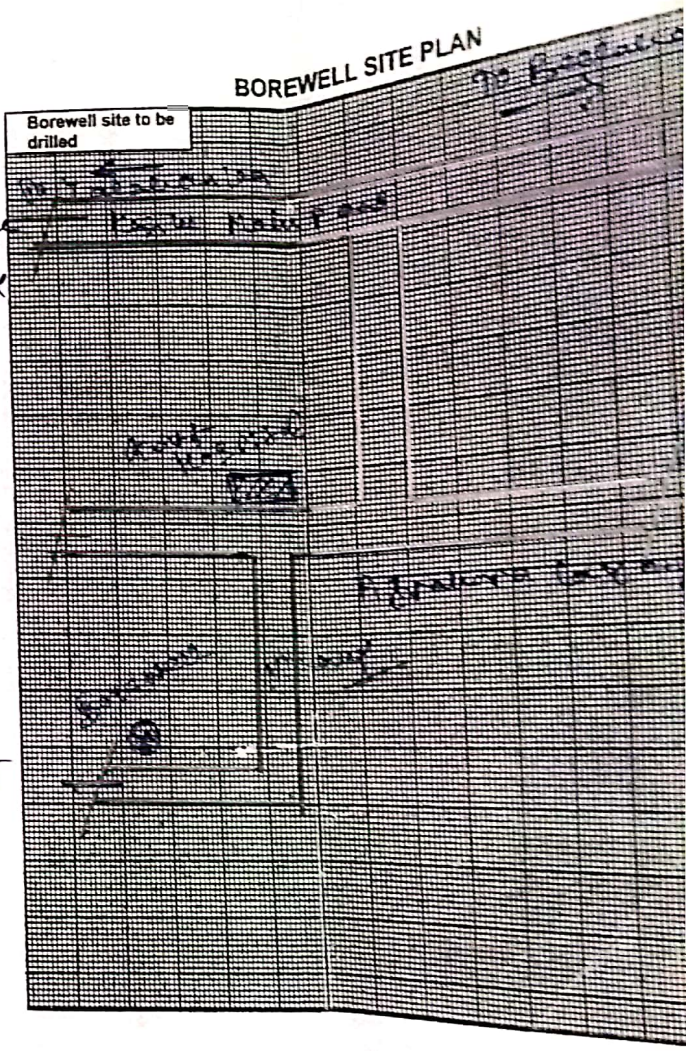

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report. I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathi
Manager / Proprietor

Signature

Scanned by CamScanner

BOREWELL

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 676

Date : 23/10/2019

1. Customer's Name and Address : AEE BBMP
   with Telephone No. Byatarayanapura Sub Division

2. Well Location : Agrahara Layout 11th cross.

3. Total Well Depth / Drilled in Ft. : 1208 feet.

4. Casing Erected in Ft. : 196 feet.

5. Water Struck at the Depth of : —

6. Total Yield (Measuring method "V" Norch : 2 inch cm / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear

8. At the Depth of : 1071 feet

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) have understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathi

Manager / Proprietor

's Signature

Scanned by CamScanner

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP

b) Location of the Site : Byrasandra Sub Div

c) Area of the land : DMR layout Kammanahalli

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Geomorphological Ward No. 05

2) Recommended Site for drilling : 1112' to 1200'

3) Total depth to be drilled :

4) Approx. casing pipe required : 190', 210'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 10 -

7) Qty. of water expected : 2 inch

8) Method of survey carried out : Geophysical

9) Remarks : 6 1/2' Dia Drill Wy

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

BOREWELL SITE PLAN

Borewell site to be drilled

Byrasandra Road

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Shalapathi
Manager / Proprietor

Party's Signature

Scanned by CamScanner

COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

Date : 25/10/2019

No. : 677

1. Customer's Name and Address with Telephone No. : AEE BBMP Byadarayanapura Zone Division

2. Well Location : BMP Layout Kathriguppe

3. Total Well Depth / Drilled in Ft. : 12th secs.

4. Casing Erected in Ft. : 203

5. Water Struck at the Depth of : —

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear

8. At the Depth of : 1106 secs

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump ✓

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathi

Manager / Proprietor

Party's Signature

Scanned by CamScanner

(1)

GROUND WATER SURVEY REPORT

OPEN WELL / BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE Byadarayanapura Sub Div
b) Location of the Site :
c) Area of the land : Kosilu Layout 7 Mane

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss rock.
2) Recommended Site for drilling : Bore well as per
3) Total depth to be drilled : 1120' - 1210'
4) Approx. casing pipe required : 190' - 210'
5) No. of water bearing Zones : - 4 -
6) No. of favourable spots marked : - 10 -
7) Qty. of water expected : 6 inch
8) Method of survey carried out : Gneiss rock.
9) Remarks : 6/12' Dia Bore well as

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಡರಹಳ್ಳಿ ಉಪ ವಿಭಾಗ
ಬಿ.ಡಿ.ಎ., ಬೆಂಗಳೂರು-24

BOREWELL SITE PLAN

Borewell site to be drilled

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well
I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathi
Manager / Proprietor

Party's Signature

Scanned by CamScanner

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

Date : 26/10/2019

No. : 678

1. Customer's Name and Address with Telephone No. : AEE BBMP Byatarayanapura Sub Division

2. Well Location : ~~Kasiba Layout 7th Cross.~~

3. Total Well Depth / Drilled in Ft. : 1210 feet.

4. Casing Erected in Ft. : 196 feet.

5. Water Struck at the Depth of :

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear clear

8. At the Depth of : 1090 feet.

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

P. Chalapathi

Manager / Proprietor

Party's Signature

Scanned by CamScanner
